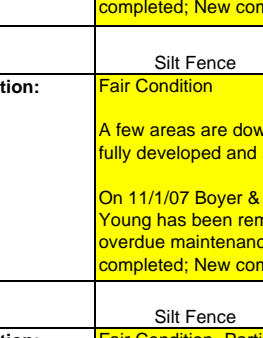


E&A - 2004.020.000				
Inspector: Mike Jacobson				Stage
Project Name:	Palisades			3
For Week Ending:	8/9/2008			
Grading:	100%			
Sanitary Sewer:	100%			
Storm Sewer:	100%			
Paving:	100%			
Seeding:	100%			
Utilities:	100%			
Overall Development:	39%			
<b>RAIN FALL AMOUNTS</b>	Amount in inches	Date inspected		
<b>Week 1</b>				
Sunday:	0.00"			
Monday	0.00"			
Tuesday	1.06"			
Wednesday	0.07"	07/16/08		
Thursday	0.19"			
Friday	0.00"	07/18/08		
Saturday	0.00"			
<b>Week 2</b>				
Sunday:	0.00"			
Monday	0.00"			
Tuesday	0.19"			
Wednesday	0.02"			
Thursday	0.39"			
Friday	0.00"			
Saturday	0.00"			
<b>Week 3</b>				
Sunday:	0.00"			
Monday	0.00"			
Tuesday	0.24"			
Wednesday	0.00"			
Thursday	0.00"			
Friday	0.00"			
Saturday	0.00"			
<b>Week 4 / 5</b>				
Sunday:	0.00"			
Monday	0.00"			
Tuesday	0.00"			
Wednesday	0.00"			
Thursday	0.00"	08/07/08		
Friday	0.00"			
Saturday	0.00"			
<b>Complaints:</b>	None			
<b>Construction Sequencing:</b>				
Which portion(s) (i.e. drainage basins) of the site have had a temporary or permanent cessation of grading, earthwork, or ground disturbance in the last 14 days?				
Entire site; grading completed and site seeded Spring 2005.				
Which portion(s) (i.e. drainage basins) of the site do not have grading, earthwork, or ground disturbance scheduled in the next 14 days? :				
Entire site; grading completed and site seeded Spring 2005.				
What temporary or permanent stabilization measures listed in this section are being implemented?				
Paving, seeding (Spring 05), dense vegetative cover				
<b>Comments:</b>				
<b>Comments:</b> Home construction is active in varies areas on site.				
<b>Findings / Corrective Actions (Date):</b>				

**Findings / Corrective Actions (Date):**

1) A few lot corners are down/damaged and needs to be retied/repared. As of inspection on 6/21/08 a few lot levels that needed maintenance has been removed and some maintenance is still needed on a few others. Due to the rains maintenance was unable to be completed; New completion date will be 7/5/08. Lot corners were removed prior to inspection on 7/18/08 by Boyer Young.  
 2) Some required maintenance in the BMP section.

Unique Name	Type	Location	Projected Install Date	Status	Maintenance	Description of Maintenance/Activity:
CE 1	Construction Entrance	N41d00m00s W96d00m00s		Removed		<b>Repairs Needed/Planned:</b>
<b>Current Condition:</b>	Removed; 2 paved entrances exist on site.					
SB 1	Sediment Basin	N41d00m00s W96d00m00s	In Place	Active	No	
<b>Current Condition:</b>	Good Condition - 30% Filled Cleaned out 06/05					
SB 2	Sediment Basin	N41d00m00s W96d00m00s	In Place	Active	No	
<b>Current Condition:</b>	Good Condition - 7% Filled Cleaned out 7/07					
SB 3	Sediment Basin	N41d00m00s W96d00m00s	In Place	Active	No	
<b>Current Condition:</b>	Good Condition - 40% Filled Cleaned out 06/05					
SB 4	Sediment Basin	N41d00m00s W96d00m00s	In Place	Active	No	
<b>Current Condition:</b>	Good Condition - 35% Filled Cleaned out 07/05					
SF 1	Silt Fence	N41d00m00s W96d00m00s	In Place	Active	Yes	
<b>Current Condition:</b>	Fair Condition  One area is down/damaged and needs to be repaired. Lot 295 has dirt piled on silt fence and it needs to be cleaned out.  Boyer Young was informed to complete maintenance by 7/25/08. Maintenance not completed as of last inspection.					
SF 2	Silt Fence	N41d00m00s W96d00m00s	In Place	Active	Yes	
<b>Current Condition:</b>	Fair Condition-  One area is full and needs to be cleaned out; a few areas down/damaged and needs to be repaired or removed due to the lots being fully developed and sodded.  On 6/20/08 the full area was cleaned out, but silt fence that needs to be removed has not been completed. Due to the rains maintenance was unable to be completed; New completion date will be 7/5/08. Maintenance not completed as of last inspection.					
SF 3		N41d00m00s W96d00m00s		Removed		
<b>Current Condition:</b>	Removed; permanent vegetation					
SF 4	Silt Fence	N41d00m00s W96d00m00s		Removed		
<b>Current Condition:</b>	Removed due to good vegetation, but will need to be reinstalled once home construction begin in this area.					
SF 5	Silt Fence	N41d00m00s W96d00m00s		Removed		
<b>Current Condition:</b>	Removed due to good vegetation, but will need to be reinstalled once home construction begin in this area.					
SF 6	Silt Fence	N41d00m00s W96d00m00s		Removed		
<b>Current Condition:</b>	Removed due to good vegetation, but will need to be reinstalled once home construction begin in this area.					
SF 7	Silt Fence	N41d00m00s W96d00m00s	In Place	Active	Yes	
<b>Current Condition:</b>	Good Condition -Partially remove due to lots be completely developed.					
SF 8	Silt Fence	N41d00m00s W96d00m00s	In Place	Active	Yes	

<b>Current Condition:</b>	Fair Condition A few areas are down and needs to be retied. A few areas needs to be removed due to the lots being fully developed and sodded. Due to the rains more maintenance is needed. A few areas are undermined and needs to be backfilled and compacted. Various areas are down/damaged and needs to be repaired.  On 11/1/07 Boyer & Young was reminded that overdue maintenance needs completed ASAP. Boyer Young has been reminded of over due maintenance. On 4/28/08 Boyer & Young was reminded that overdue maintenance needs completed ASAP. Due to the rains maintenance was unable to be completed; New completion date will be 7/5/08. Maintenance not completed as of last inspection.				
SF 9	Silt Fence	N41d00m00s W96d00m00s	In Place	Active	Yes
<b>Current Condition:</b>	Fair Condition A few areas are down and needs to be retied. One area needs to be removed due to the lots being fully developed and sodded.  On 11/1/07 Boyer & Young was reminded that overdue maintenance needs completed ASAP. Boyer Young has been reminded of over due maintenance. On 4/28/08 Boyer & Young was reminded that overdue maintenance needs completed ASAP. Due to the rains maintenance was unable to be completed; New completion date will be 7/5/08. Maintenance not completed as of last inspection.				
SF 10	Silt Fence	N41d00m00s W96d00m00s	In Place	Active	No
<b>Current Condition:</b>	Fair Condition- Partially removed due to lot development. Silt fence was removed behind sodded lots prior to inspection on 7/16/08.  One area is full and needs to be cleaned out; Due to the rain more maintenance is needed. One area is blown out and needs to be replaced. One area is damaged and needs to be repaired.  On 11/1/07 Boyer & Young was reminded that overdue maintenance needs completed ASAP. Boyer Young has been reminded of over due maintenance. On 4/28/08 Boyer & Young was reminded that overdue maintenance needs completed ASAP. Due to the rains maintenance was unable to be completed; New completion date will be 7/5/08. Maintenance not completed as of last inspection.				
ST 1	Silt Trap	N41d00m00s W96d00m00s		Removed	
<b>Current Condition:</b>	Removed; berm constructed and area matted and seeded.				
STR	Streets	N41d00m00s W96d00m00s	In Place	Active	No
<b>Current Condition:</b>	Good Condition - No major signs of track off.				
<b>Inspector Signature:</b>			<b>Reviewed By:</b> 
